


RUE: Nordon PL - AKL - 20, Unit
A(NGA-ROW) - CallPlus (135838)

NGA Designer: Chris Yang
Contact: 09-9281554

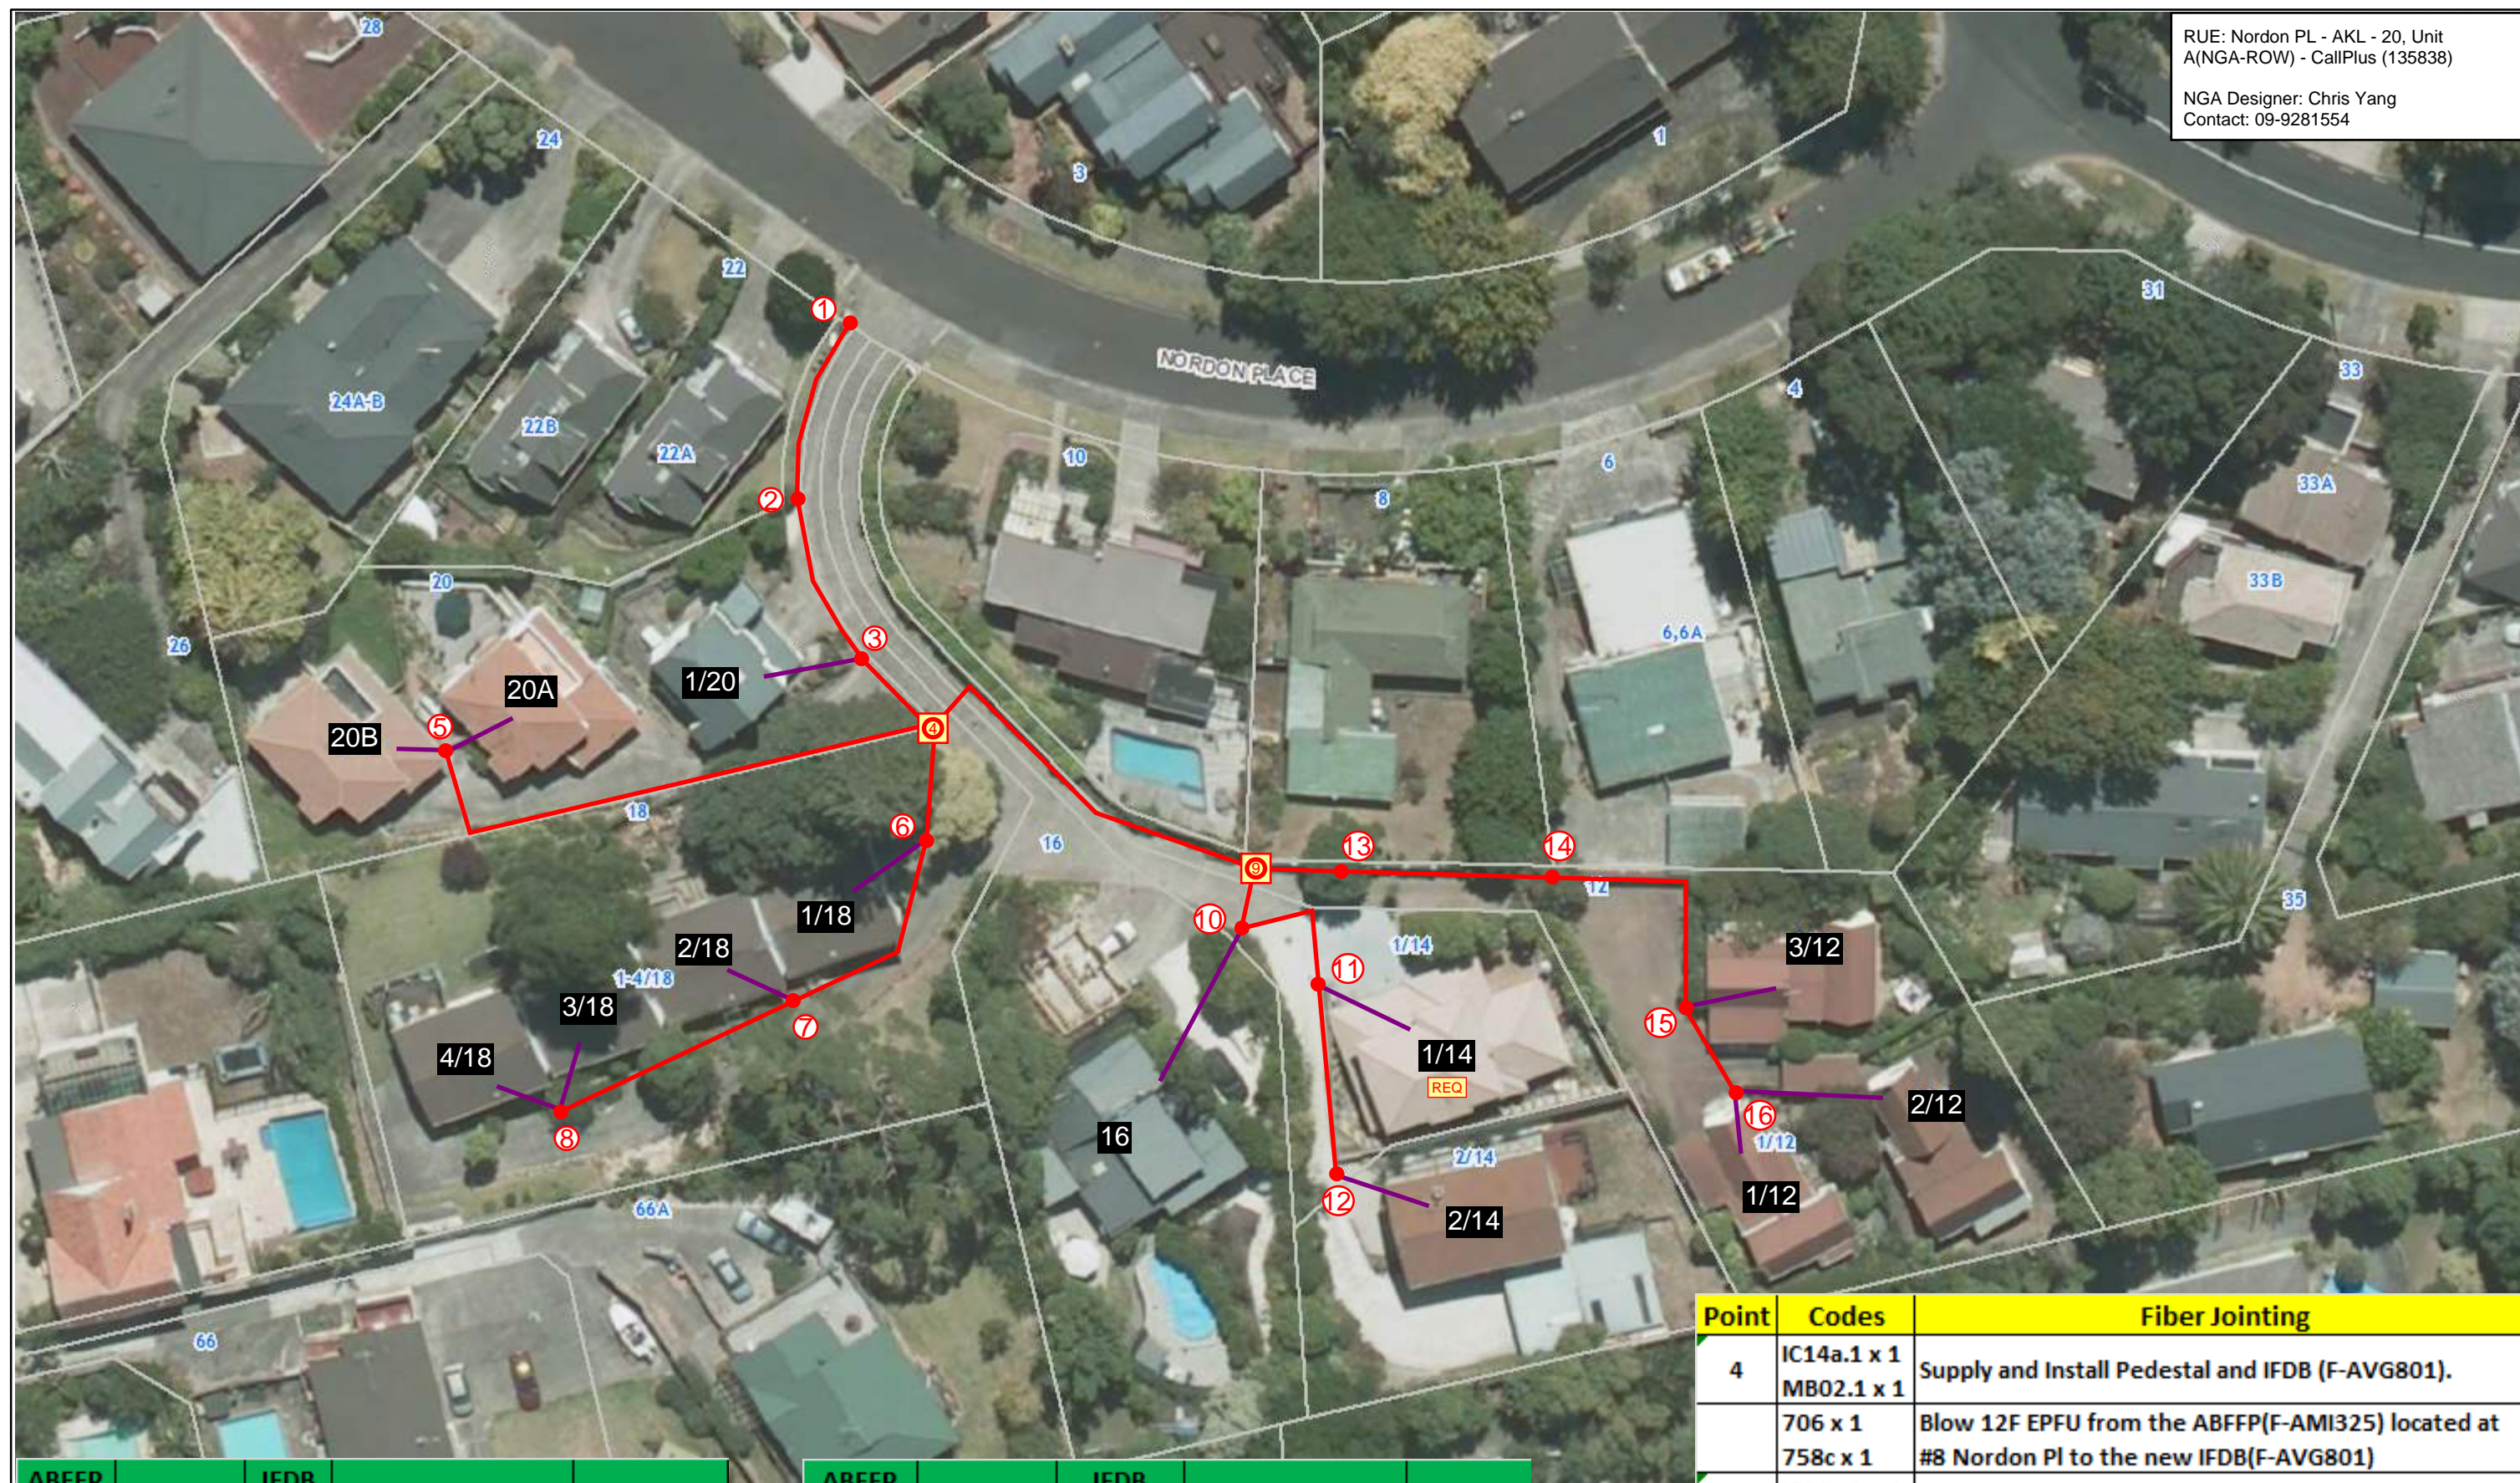

ABFFP Fibres	IFDB	IFDB Fibres	Address	Lot Number
85..86	F-AVG801	1..2	1/18 Nordon Pl	20A
87..88	F-AVG801	3..4	1/18 Nordon Pl	20B
89..90	F-AVG801	5..6	1/18 Nordon Pl	Unit 1/ 18
91..92	F-AVG801	7..8	1/18 Nordon Pl	Unit 2/ 18
93..94	F-AVG801	9..10	1/18 Nordon Pl	Unit 3/ 18
95..96	F-AVG801	11..12	1/18 Nordon Pl	Unit 4/ 18

ABFFP Fibres	IFDB	IFDB Fibres	Address	Lot Number
73..74	F-AVG802	1..2	1/14 Nordon Pl	16
75..76	F-AVG802	3..4	1/14 Nordon Pl	Unit 1/14
77..78	F-AVG802	5..6	1/14 Nordon Pl	Unit 2/14
79..80	F-AVG802	7..8	1/14 Nordon Pl	Unit 3/12
81..82	F-AVG802	9..10	1/14 Nordon Pl	Unit 1/12
83..84	F-AVG802	11..12	1/14 Nordon Pl	Unit 2/12

Point	Codes	Fiber Jointing
4	IC14a.1 x 1 MB02.1 x 1	Supply and Install Pedestal and IFDB (F-AVG801).
	706 x 1	Blow 12F EPFU from the ABFFP(F-AMI325) located at #8 Nordon Pl to the new IFDB(F-AVG801)
9	IC14a.1 x 1 MB02.1 x 1	Supply and Install Pedestal and IFDB (F-AVG802).
	706 x 1	Blow 12F EPFU from the ABFFP(F-AMI325) located at #8 Nordon Pl to the new IFDB(F-AVG802)
F-AVG801		
F-AMI325 : 85-96		
F-AVG802		
F-AMI325: 73-84		

Points	Codes	Civil
1	C04 x 2 C12M x 3	Trench in Grass for 2m OSB and locate Drop off, Connect 3 x Ruggedized
1-2	D01 x 15	Trench in grass for 15m, Lay 3 x Ruggedized
2-3	D03 x 13	Micro trench in concrete for 13m, Lay 3 x Ruggedized
3		Leave 1 x Ruggedized for #1/20
3-4	D03 x 6	Micro trench in concrete for 6m, Lay 2 x Ruggedized
4		Install a new pedestal and IFDB (to be done by the jointer)
4-5	D03 x 35	Micro trench in concrete for 35m, Lay 2 x Ruggedized
5		Leave 2 x Ruggedized for #20A and #20B
4-6	D01 x 7	Trench in grass for 7m, Lay 4 x Ruggedized
6		Leave 1 x Ruggedized for #1/18
6-7	D03 x 20	Micro trench in concrete for 20m, Lay 3 x Ruggedized
7		Leave 1 x Ruggedized for #2/18
7-8	D03 x 25	Micro trench in concrete for 25m, Lay 2 x Ruggedized
8		Leave 2 x Ruggedized for #3/18 and #4/18
4-9	D03 x 30	Micro trench in concrete for 30m, Lay 1 x Ruggedized
9		Install a new pedestal and IFDB (to be done by the jointer)
9-10	D03 x 4	Micro trench in concrete for 4m, Lay 3 x Ruggedized
10		Leave 1 x Ruggedized for #16
10-11	D03 x 9	Micro trench in concrete for 9m, Lay 2 x Ruggedized
11		Leave 1 x Ruggedized for #1/14
11-12	D01 x 13 G06 x 8	Trench in garden for 13m, Lay 1 x Ruggedized
12		Leave 1 x Ruggedized for #2/14
9-13	D03 x 14	Micro trench in concrete for 14m, Lay 3 x Ruggedized
13-14	733 x 12 MD1A x 12 707 x 3	Clip 1 x 20mm duct to wall for 12m, Haul 3 x Ruggedized
14-15	733 x 19 MD1A x 19	Clip 1 x 20mm duct to fence for 19m, Haul 3 x Ruggedized
15		Leave 1 x Ruggedized for #3/12
15-16	D03 x 10	Micro trench in concrete for 10m, Lay 2 x Ruggedized
16		Leave 2 x Ruggedized for #1/12 and #2/12
